

As Drilled SCHEMATIC



ELEVATION
RESOURCES

Well Name: University 1-27 South Unit #3H
Formation: Devonian
County, St: Andrews, TX
SHL: 2575' FSL 200' FEL, Sec. 27, Blk 1, University Lands Survey
BHL: 98' FSL 213' FEL, Sec. 34, Blk 1, University Lands Survey
API #: 42-003-47423
Spud: 12/3/16
Rig Down: 1/21/17
TD: 18,730'

Drilling Engineer: Jason L. Kincaid
Completion Engineer: Mark Solari

GL: 3125'
KB: 25'
RKB: 3150'

FORMATION TOPS	TVD	MD
Rustler	1,830	
Yates	3,092	
San Andres	4,862	
Base San Andres	5,775	
Clearfork	6,614	
Wolfcamp	8,438	
Strawn	9,649	
Lower Barnett	10,280	
Woodford Shale	10,840	
Devonian	10,934	
Target Depth	11,060	

DIRECTIONAL DETAILS							
TARGET	MD	TVD	(θ)	AZM	N/S	E/W	VS
KOP	10675	10675					
Landing Pt							
TD Lateral							

CASING DETAIL										
	Conn	Size	Wt	Grade	*Burst*	Collapse	Start	End	Length	TD
Surface	STC	13 3/8	54.5	J-55	2184	1130	0	1586	1586	1620
Intermediate	LTC	9 5/8	40	J-55	3160	2570	0	2845	2845	7180
Intermediate	LTC	9 5/8	40	HCK-55	3160	4230	2845	7010	4165	7180
Intermediate II	LTC	7	26	HCL-80	8512	7480	0	6849	6849	11455
Intermediate II	LTC	7	26	HCL-80	8512	7480	6849	11414	4565	11455
Production		4 1/2	11.6	P-110			10559	18728	8169	18730


*80%

Tubing Detail: As of: 2/28/17:

KB= 25'
 307 jts 2-7/8" 6.5# L-80 Tbg.
 1- Sub. Pump
 EOP @ 10,1130'

Rod Detail: As of: :

No rods in hole

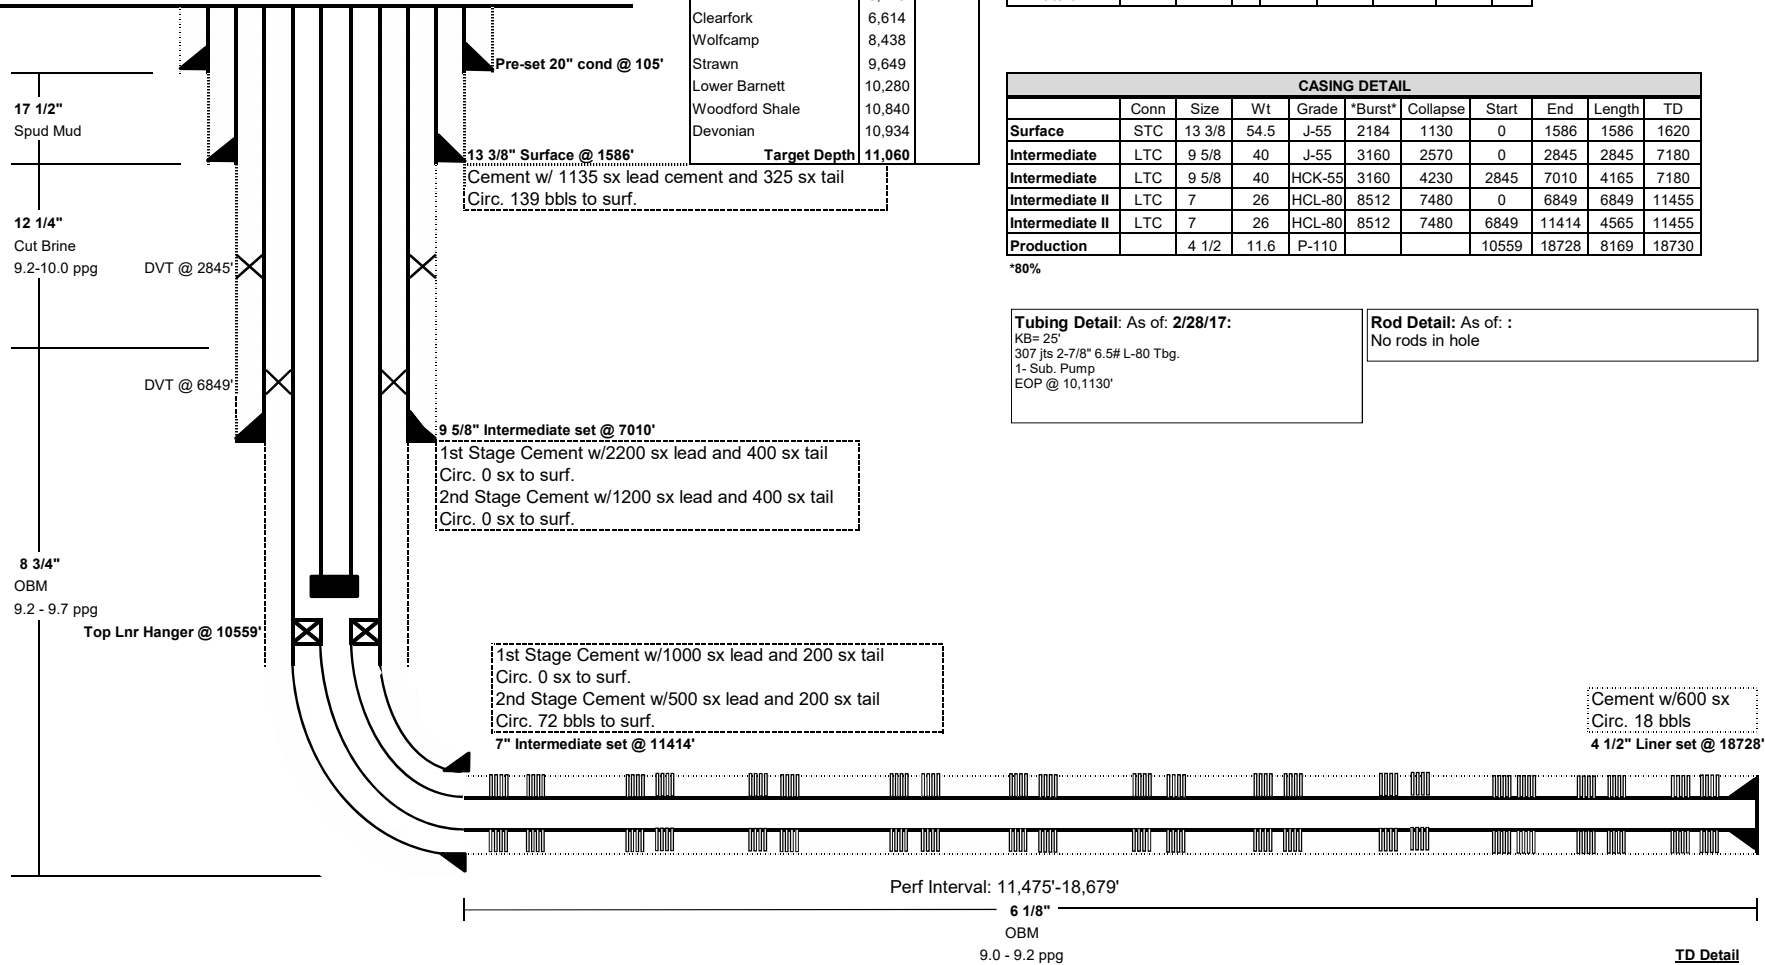

TD Detail

MD 18730'

TVD 11388'

Inc: 90°

Drilling Fluids	Build Section	Tool	Lateral Section	Tool	Liner System	Cement	AFE No.	Permit No.	API	Prepared By: Jason L. Kincaid
Dynamic	Gyrodat	PDM	Gyrodata	PDM	Cemented	Trans-Tex	15116	805478	42-003-47423	Date: 17-Aug-15



PERFORATIONS SUMMARY

DATE	August 1, 2015	SUPERVISOR	
WELL NAME	Universtiy 1-27 #2-H	ENGINEER	Mark Solari
PROSPECT/FIELD	University	STATE	Texas
LEASE	Universtiy 1-27		

PERFORATIONS						
Zone	Method	Top TD	Btm TD	Density	Hole Size	
Stage 1	Wireline	18,675	18,679	6	0.41	
0	Wireline	18,475	18,479	6	0.41	
Stage 2	Wireline	18,275	18,279	6	0.41	
0	Wireline	18,075	18,079	6	0.41	
Stage 3	Wireline	17,925	17,929	6	0.41	
0	Wireline	17,775	17,779	6	0.41	
Stage 4	Wireline	17,620	17,624	6	0.41	
0	Wireline	17,475	17,479	6	0.41	
Stage 5	Wireline	17,325	17,329	6	0.41	
0	Wireline	17,175	17,179	6	0.41	
Stage 6	Wireline	17,025	17,029	6	0.41	
0	Wireline	16,870	16,874	6	0.41	
Stage 7	Wireline	16,725	16,729	6	0.41	
0	Wireline	16,575	16,579	6	0.41	
Stage 8	Wireline	16,425	16,429	6	0.41	
0	Wireline	16,275	16,279	6	0.41	
Stage 9	Wireline	16,125	16,129	6	0.41	
0	Wireline	15,975	15,979	6	0.41	
Stage 10	Wireline	15,825	15,829	6	0.41	
0	Wireline	15,675	15,679	6	0.41	
Stage 11	Wireline	15,525	15,529	6	0.41	
0	Wireline	15,365	15,369	6	0.41	
Stage 12	Wireline	15,225	15,229	6	0.41	
0	Wireline	15,075	15,079	6	0.41	
Stage 13	Wireline	14,925	14,929	6	0.41	
0	Wireline	14,775	14,779	6	0.41	
Stage 14	Wireline	14,621	14,625	6	0.41	
0	Wireline	14,475	14,479	6	0.41	
Stage 15	Wireline	14,330	14,334	6	0.41	
0	Wireline	14,175	14,179	6	0.41	
Stage 16	Wireline	14,025	14,029	6	0.41	
0	Wireline	13,870	13,874	6	0.41	
Stage 17	Wireline	13,725	13,729	6	0.41	
0	Wireline	13,570	13,574	6	0.41	
Stage 18	Wireline	13,425	13,429	6	0.41	
0	Wireline	13,265	13,269	6	0.41	
Stage 19	Wireline	13,425	13,429	6	0.41	
0	Wireline	13,265	13,269	6	0.41	
Stage 20	Wireline	12,825	12,829	6	0.41	
0	Wireline	12,660	12,664	6	0.41	
Stage 21	Wireline	12,525	12,529	6	0.41	
0	Wireline	12,368	12,372	6	0.41	
Stage 22	Wireline	12,225	12,229	6	0.41	
0	Wireline	12,082	12,086	6	0.41	
Stage 23	Wireline	11,925	11,929	6	0.41	
0	Wireline	11,775	11,779	6	0.41	

Stage 24	Wireline	11,620	11,625	6	0.41
0	Wireline	11,475	11,479	6	0.41
0					
www.wellez.com WellEz Information Management LLC ver_10.21.13cv					
